


Attachment C - Installation Schedule Town of Mamaroneck

ID	Task Name	Duration	Start	Finish	1st Half		1st Half		1st Half		1st Half	
					Qtr 1	Qtr 3	Qtr 1	Qtr 3	Qtr 1	Qtr 3	Qtr 1	Qtr 3
1	Town of Mamaroneck	195 days?	Wed 4/2/14	Tue 12/30/14	Town of Mamaroneck							
2	Signed Contract	0 days	Wed 4/2/14	Wed 4/2/14	Signed Contract							
3	Permits	0 days	Wed 4/9/14	Wed 4/9/14	4/2							
4	ECM 1 - Lighting Retrofit and Vending Misers	73 days	Fri 5/30/14	Mon 9/8/14	4/9							
5	Town Center	12 days	Fri 5/30/14	Fri 6/13/14	ECM 1 - Lighting Retrofit and Vending Misers							
6	Fire Headquarters	5 days	Mon 6/16/14	Fri 6/20/14	Town Center							
7	Ice Rink	5 days	Tue 9/2/14	Mon 9/8/14	Fire Headquarters							
8	Parking Garage	5 days	Mon 6/23/14	Fri 6/27/14	Ice Rink							
9	ECM 2 - Street Lighting Upgrades	70 days	Mon 9/15/14	Fri 12/19/14	Parking Garage							
10	ECM 3 - Boiler Plant Upgrade	24 days	Mon 6/30/14	Thu 7/31/14	ECM 2 - Street Lighting Upgrades							
11	ECM 4 - Ice Rink Chiller Plant	103 days	Thu 4/10/14	Fri 8/29/14	ECM 3 - Boiler Plant Upgrade							
12	Order Chiller/HVAC Equipment	73 days	Thu 4/10/14	Fri 7/18/14	ECM 4 - Ice Rink Chiller Plant							
13	Existing dasher board removal/refrig demo	21 days	Mon 5/5/14	Sun 6/1/14	Order Chiller/HVAC Equipment							
14	Install new sand, sub surface, glycol tubing	52 days	Mon 6/2/14	Tue 8/12/14	Existing dasher board removal/refrig demo							
15	Install new dasher boards	16 days	Fri 8/1/14	Fri 8/22/14	Install new sand, sub surface, glycol tubing							
16	Drive piles, relocate water main, excavate for slab	16 days	Mon 6/2/14	Mon 6/23/14	Install new dasher boards							
17	Pour Concrete, install grade beams	1 day	Tue 6/24/14	Tue 6/24/14	Drive piles, relocate water main, excavate for slab							
18	Set building steel and exterior	6 days	Tue 7/8/14	Tue 7/15/14	Pour Concrete, install grade beams							
19	Electrical Install for new plant	30 days	Mon 7/21/14	Fri 8/29/14	Set building steel and exterior							
20	Refrigeration equipment/piping install	29 days	Mon 7/21/14	Thu 8/28/14	Electrical Install for new plant							
21	ECM 5 - BMS Upgrades	70 days	Mon 6/2/14	Fri 9/5/14	Refrigeration equipment/piping install							
22	Town Center	20 days	Mon 6/2/14	Fri 6/27/14	ECM 5 - BMS Upgrades							
23	Ice Rink	14 days	Tue 8/12/14	Fri 8/29/14	Town Center							
24	Fire Station	5 days	Mon 9/1/14	Fri 9/5/14	Ice Rink							
25	ECM 6 - Building Envelope Upgrades	13 days	Mon 4/28/14	Wed 5/14/14	Fire Station							
26	Town Center	5 days	Mon 4/28/14	Fri 5/2/14	ECM 6 - Building Envelope Upgrades							
27	Fire Station	4 days	Mon 5/5/14	Thu 5/8/14	Town Center							
28	Ice Rink	4 days	Fri 5/9/14	Wed 5/14/14	Fire Station							
29	ECM 7 - Pipe Insulation	8 days	Mon 5/19/14	Wed 5/28/14	Ice Rink							
30	ECM 8 - Window Film	9 days?	Fri 6/13/14	Wed 6/25/14	ECM 7 - Pipe Insulation							
31	Town Center	6 days?	Fri 6/13/14	Fri 6/20/14	Town Center							
32	Fire Station	3 days	Mon 6/23/14	Wed 6/25/14	Fire Station							
33	ECM 9 - Replace Condensing Units	55 days	Mon 9/15/14	Fri 11/28/14	Ice Rink							
34	ECM 10 - Generator Upgrade	21 days	Wed 10/1/14	Wed 10/29/14	ECM 9 - Replace Condensing Units							
35	Walk throughs	20 days	Mon 11/17/14	Fri 12/12/14	ECM 10 - Generator Upgrade							

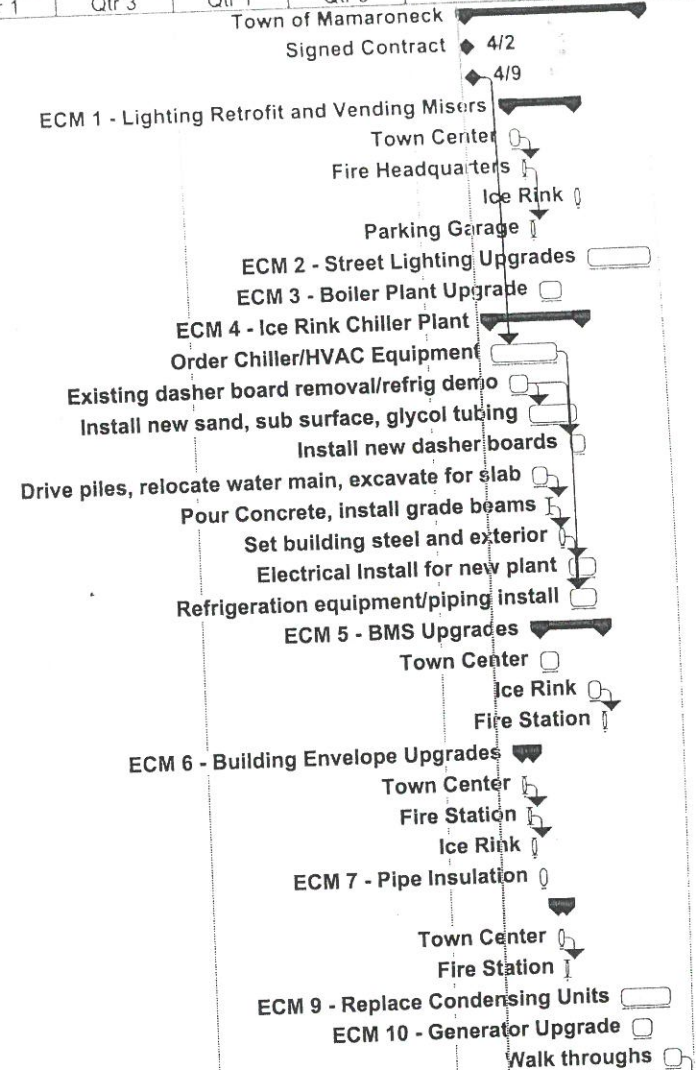

Project: Town of Mamaroneck

Task

Split

Progress

Milestone

Summary

Project Summary

External Tasks

External MileTask

Split
